


# Grand Teton Music Festival's Walk Festival Hall Preservation Project Complete Summer 2007

Progress Report for Week 28 ~ 3.16.07

PROJECT SCHEDULE

<b>June 07</b> PROJECT COMPLETE Landscaping Memorial Garden	
<b>May 07</b> Sound Wall Concrete sidewalks Exterior decking Steel shingles & siding	
<b>April 07</b> Wood siding Remobilize for external work Stone veneer	
<b>March 07</b> Complete painting Interior flooring & finishes Stage flooring	
<b>February 07</b> Mechanical systems Wall ceilings Start painting stage	
<b>January 07</b> Complete overhead Work in hall/stage Continue mechanical work New walls & ceilings	
<b>December 06</b> Interior framing & insulation Mechanical upgrade Interior demolition	
<b>November 06</b> Demobilize for start of ski season Re-roof lower Portion Panel completion	
<b>Oct 06</b> Start upper roof panels Start new vestibules & washrooms	
<b>Sept 06</b> Start wood trim Erect wall panels Demolition	

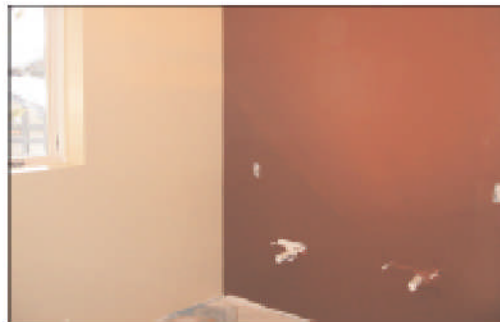

Back stage bathrooms are being painted.



Stage Hands area has been reframed to incorporate building inspector's requests.



Back stage area is being painted the color of "Tarragon"



HVAC ducting has been framed and enclosed in a soffit which is now being painted.

NEXT WEEK: Painting continues

The Walk Festival Hall Preservation Project is a collaboration of [Berlin Architects](#), [Big-D Signature](#), [Jaffe-Holden Acoustics](#), and [AK&A Project Management](#).  
For more information contact the Grand Teton Music Festival at 307.733.3050.
