

Grand Teton Music Festival's Walk Festival Hall Preservation Project Complete Summer 2007

Progress Report for Week 33 ~ 4.20.07

PROJECT SCHEDULE


June 07 PROJECT COMPLETE Landscaping Memorial Garden	
May 07 Sound Wall Concrete sidewalks Exterior decking Steel shingles & siding	
April 07 Wood siding, Vestibules Remobilize for external work, New deck roof, Stone veneer	
March 07 Complete painting Interior flooring & finishes, Bkstage insulation, Stage flooring	
February 07 Mechanical systems Wall ceilings Start painting stage	
January 07 Complete overhead Work in hall/stage Continue mechanical work New walls & ceilings	
December 06 Interior framing & insulation Mechanical upgrade Interior demolition	
November 06 Demobilize for start of ski season Re-roof lower Portion Panel completion	
October 06 Start upper roof panels Start new vestibules & washrooms	
September 06 Start wood trim Erect wall panels Demolition	



Steel for the new ticket booth is being erected.



The footing for the new "Sound Bench" has been poured. The bench will be the centerpiece of a new memorial garden.

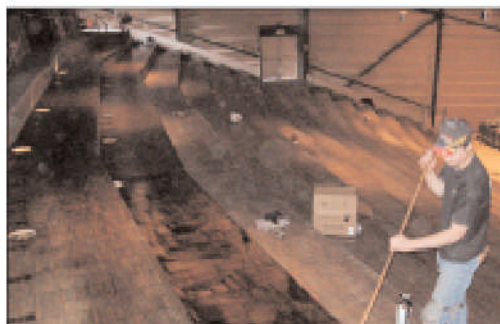

The parquet floors are being refinished. When complete, the seating will be reinstalled.



Painting of the performance hall is almost complete. The new stage floor installation begins soon!

NEXT WEEK: Installation

The Walk Festival Hall Preservation Project is a collaboration of **Berlin Architects**, **Big-D Signature**, **Jaffe-Holden Acoustics**, and **AK&A Project Management**.
For more information contact the Grand Teton Music Festival at 307.733.3050.
