

Grand Teton Music Festival's Walk Festival Hall Preservation Project Complete Summer 2007

Progress Report for Week 34 ~ 4.27.07

PROJECT SCHEDULE


June 07 PROJECT COMPLETE Landscaping Memorial Garden	
May 07 Sound Wall Concrete sidewalks Exterior decking Steel shingles & siding	
April 07 Wood siding, Vestibules Remobilize for external work, New deck roof, Stone veneer	
March 07 Complete painting Interior flooring & finishes, Bkstage insulation, Stage flooring	
February 07 Mechanical systems Wall ceilings Start painting stage	
January 07 Complete overhead Work in hall/stage Continue mechanical work New walls & ceilings	
December 06 Interior framing & insulation Mechanical upgrade Interior demolition	
November 06 Demobilize for start of ski season Re-roof lower Portion Panel completion	
October 06 Start upper roof panels Start new vestibules & washrooms	
September 06 Start wood trim Erect wall panels Demolition	



Access to the new "Percussion Storage" room was cut through a cinderblock wall and the area has been framed.



Chairs are being reinstalled over the refinished parquet flooring and the stage floor material is being readied for installation to start next week.

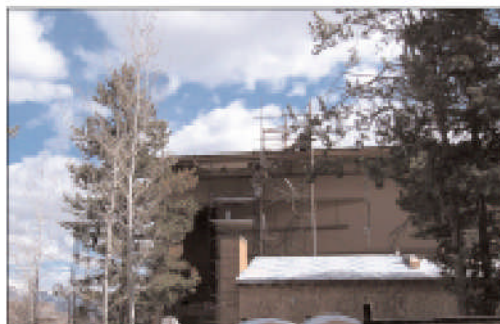

New concrete with an integral ice melt system is being installed outside the area where the new "north vestibule" will stand.



The steel for the new ticket booth is all in place.

NEXT WEEK: Installation

The Walk Festival Hall Preservation Project is a collaboration of **Berlin Architects**, **Big-D Signature**, **Jaffe-Holden Acoustics**, and **AK&A Project Management**.
 For more information contact the Grand Teton Music Festival at 307.733.3050.
