

Grand Teton Music Festival's Walk Festival Hall Preservation Project Complete Summer 2007


Progress Report for Week 42 ~ 6.22.07

PROJECT SCHEDULE

June 07 PROJECT COMPLETE Landscaping Memorial Garden	
May 07 Sound Wall Concrete sidewalks Exterior decking Steel shingles & siding	
April 07 Wood siding, Vestibules Remobilize for external work, New deck roof, Stone veneer	
March 07 Complete painting Interior flooring & finishes, Bkstage insulation, Stage flooring	
February 07 Mechanical systems Wall ceilings Start painting stage	
January 07 Complete overhead Work in hall/stage Continue mechanical work New walls & ceilings	
December 06 Interior framing & insulation Mechanical upgrade Interior demolition	
November 06 Demobilize for start of ski season Re-roof lower Portion Panel completion	
October 06 Start upper roof panels Start new vestibules & washrooms	
September 06 Start wood trim Erect wall panels Demolition	



Cabinetry and countertops have been installed in the Musician's Lounge. Appliances will arrive shortly.

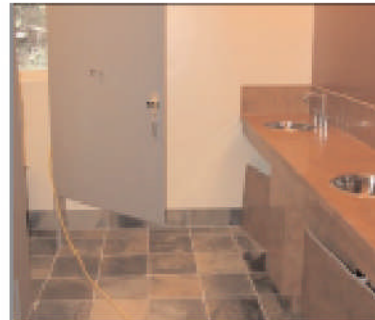

The backstage restrooms are almost ready to go. Mirrors and accessories are all that's left to install.



Landscaping is going in around the site.



Steel shingles are being installed on the restroom wall near the concession area. This wall will eventually highlight the names of donors.

NEXT WEEK: Landscaping continues

The Walk Festival Hall Preservation Project is a collaboration of [Berlin Architects](#), [Big-D Signature](#), [Jaffe-Holden Acoustics](#), and [AK&A Project Management](#).

For more information contact the Grand Teton Music Festival at 307.733.3050.
